

972-979-7346

www.sginspectionservices.com office@sginspectionservices.com



INSPECTED FOR

Bob Buyer 69 Joyfull Way Dallas, TX 75206

February 20, 2020

972-979-7346

office @sginspectionservices.com

PROPERTY INSPECTION REPORT

Prepared For:	Bob Buyer	
•	(Name of Client)	
Concerning:	_69 Joyfull Way, Dallas, TX 75206	
	(Address or Other Identification of Inspected Property)	
By:	Nathan Ross, Lic #20282	02/20/2020
	(Name and License Number of Inspector)	(Date)
	(Name, License Number of Sponsoring Inspector)	

PURPOSE, LIMITATIONS AND INSPECTOR / CLIENT RESPONSIBILITIES

This property inspection report may include an inspection agreement (contract), addenda, and other information related to property conditions. If any item or comment is unclear, you should ask the inspector to clarify the findings. It is important that you carefully read ALL of this information.

This inspection is subject to the rules ("Rules") of the Texas Real Estate Commission ("TREC"), which can be found at www.trec.texas.gov.

The TREC Standards of Practice (Sections 535.227-535.233 of the Rules) are the minimum standards for inspections by TREC-licensed inspectors. An inspection addresses only those components and conditions that are present, visible, and accessible at the time of the inspection. While there may be other parts, components or systems present, only those items specifically noted as being inspected were inspected. The inspector is NOT required to turn on decommissioned equipment, systems, utility services or apply an open flame or light a pilot to operate any appliance. The inspector is NOT required to climb over obstacles, move furnishings or stored items. The inspection report may address issues that are code-based or may refer to a particular code; however, THIS IS NOT A CODE COMPLIANCE INSPECTION and does NOT verify compliance with manufacturer's installation instructions. THE INSPECTION DOES NOT IMPLY INSURABILITY OR WARRANTABILITY OF THE STRUCTURE OR ITS COMPONENTS. Although some safety issues may be addressed in this report, THIS REPORT IS NOT A SAFETY / CODE INSPECTION, and the inspector is NOT required to identify all potential hazards.

In this report, the inspector shall indicate, by checking the appropriate boxes on the form, whether each item was inspected, not inspected, not present or deficient and explain the findings in the corresponding section in the body of the report form. The inspector must check the Deficient (D) box if a condition exists that adversely and materially affects the performance of a system or component or constitutes a hazard to life, limb or property as specified by the TREC Standards of Practice. General deficiencies include inoperability, material distress, water penetration, damage, deterioration, missing components, and unsuitable installation. Comments may be provided by the inspector whether or not an item is deemed deficient. The inspector is not required to prioritize or emphasize the importance of one deficiency over another.

Some items reported may be considered life-safety upgrades to the property. For more information, refer to Texas Real Estate Consumer Notice Concerning Recognized Hazards or Deficiencies below.

THIS PROPERTY INSPECTION IS NOT A TECHNICALLY EXHAUSTIVE INSPECTION OF THE STRUCTURE, SYSTEMS OR COMPONENTS. THE INSPECTION MAY NOT REVEAL ALL DEFICIENCIES. A REAL ESTATE INSPECTION HELPS TO REDUCE SOME OF THE RISK INVOLVED IN PURCHASING A HOME, BUT IT CANNOT ELIMINATE THESE RISKS, NOR CAN THE INSPECTION ANTICIPATE FUTURE EVENTS OR CHANGES IN PERFORMANCE DUE TO CHANGES IN USE OR OCCUPANCY. It is recommended that you obtain as much information as is available about this property, including any seller's disclosures, previous inspection reports, engineering reports, building/remodeling permits, and reports performed for or by relocation companies, municipal inspection departments, lenders, insurers, and appraisers. You should also attempt to determine whether repairs, renovation, remodeling, additions, or other such activities have taken place at this property. It is not the inspection's responsibility to confirm that information obtained from these sources is complete or accurate or that this inspection is consistent with the opinions

Promulgated by the Texas Real Estate Commission (TREC), P.O. Box 12188, Austin, TX 78711-2188 (512) 936-3000 (http://www.trec.texas.gov).

expressed in previous or future reports.

verify that proper repairs have been made.

ITEMS IDENTIFIED IN THE REPORT DO NOT OBLIGATE ANY PARTY TO MAKE REPAIRS OR TAKE OTHER ACTIONS, NOR IS THE PURCHASER REQUIRED TO REQUEST THAT THE SELLER TAKE ANY ACTION. When a deficiency is reported, it is the client's responsibility to obtain further evaluations and/or cost estimates from qualified service professionals. Any such follow-up should take place prior to the expiration of any time limitations such as option periods. Evaluations by qualified tradesmen may lead to the discovery of additional deficiencies which may involve additional repair costs. Failure to address deficiencies or comments noted in this report may lead to further damage of the structure or systems and add to the original repair costs. The inspector is not required to provide follow-up services to

Property conditions change with time and use. For example, mechanical devices can fail at any time, plumbing gaskets and seals may crack if the appliance or plumbing fixture is not used often, roof leaks can occur at any time regardless of the apparent condition of the roof, and the performance of the structure and the systems may change due to changes in use or occupancy, effects of weather, etc. These changes or repairs made to the structure after the inspection may render information contained herein obsolete or invalid. This report is provided for the specific benefit of the client named above and is based on observations at the time of the inspection. If you did not hire the inspector yourself, reliance on this report may provide incomplete or outdated information. Repairs, professional opinions or additional inspection reports may affect the meaning of the information in this report. It is recommended that you hire a licensed inspector to perform an inspection to meet your specific needs and to provide you with current information concerning this property.

TEXAS REAL ESTATE CONSUMER NOTICE CONCERNING HAZARDS OR DEFICIENCIES

Each year, Texans sustain property damage and are injured by accidents in the home. While some accidents may not be avoidable, many other accidents, injuries, and deaths may be avoided through the identification and repair of certain hazardous conditions. Examples of such hazards include:

- malfunctioning, improperly installed or missing ground fault circuit protection (GFCI) devices for electrical receptacles in garages, bathroom, kitchens, and exterior areas;
- malfunctioning arc fault protection (AFCI) devices;
- ordinary glass in locations where modern construction techniques call for safety glass;
- the lack of fire safety features, such as smoke alarms, fire-rated doors in certain locations, and functional emergency escape and rescue openings in bedrooms;
- malfunctioning carbon monoxide alarms;
- excessive spacing between balusters on stairways and porches;
- improperly installed appliances;
- improperly installed or defective safety devices
- lack of electrical bonding and grounding; and
- lack of bonding on gas piping, including corrugated stainless steel tubing (CSST).

To ensure that consumers are informed of hazards such as these, the Texas Real Estate Commission (TREC) has adopted Standards of Practice requiring licensed inspectors to report these conditions as "Deficient" when performing an inspection for a buyer or seller, if they can be reasonably determined.

These conditions may not have violated building codes or common practices at the time of the construction of the home, or they may have been "grandfathered" because they were present prior to the adoption of codes prohibiting such conditions. While the TREC Standards of Practice do not require inspectors to perform a code compliance inspection, TREC considers the potential for injury or property loss from the hazards addressed in the Standards of Practice to be significant enough to warrant this notice.

Contract forms developed by TREC for use by its real estate licensees also inform the buyer of the right to have the home inspected and can provide an option clause permitting the buyer to terminate the contract within a specified time. Neither the Standards of Practice nor the TREC contract forms requires a seller to remedy conditions revealed by an inspection. The decision to correct a hazard or any deficiency identified in an inspection report is left to the parties to the contract for the sale or purchase of the home.

INFORMATION INCLUDED UNDER "ADDITIONAL INFORMATION PROVIDED BY INSPECTOR", OR PROVIDED AS AN ATTACHMENT WITH THE STANDARD FORM, IS NOT REQUIRED BY THE COMMISSION AND MAY CONTAIN CONTRACTUAL TERMS BETWEEN THE INSPECTOR AND YOU, AS THE CLIENT. THE COMMISSION DOES NOT REGULATE CONTRACTUAL TERMS BETWEEN PARTIES. IF YOU DO NOT UNDERSTAND THE EFFECT OF ANY CONTRACTUAL TERM CONTAINED IN THIS SECTION OR ANY ATTACHMENTS, CONSULT AN ATTORNEY.

ADDITIONAL INFORMATION PROVIDED BY INSPECTOR

Inspection Time In: 9:45 am Time Out: 12 pm Property was: Vacant Building Orientation (For Purpose Of This Report Front Faces): South

Weather Conditions During Inspection: Cloudy Overcast Outside temperature during inspection: 60 ° or Below Degrees

Parties present at inspection: Contractors

THIS REPORT IS PAID AND PREPARED FOR THE EXCLUSIVE USE BY Bob Buyer. THIS COPYRIGHTED REPORT IS NOT VALID WITHOUT THE SIGNED INSPECTION AGREEMENT.

THIS REPORT IS NOT TRANSFERABLE FROM CLIENT NAMED ABOVE.

SCOPE OF INSPECTION

These standards of practice define the minimum levels of inspection required for substantially completed residential improvements to real property up to four dwelling units. A real estate inspection is a non-technically exhaustive, limited visual survey and basic performance evaluation of the systems and components of a building using normal controls and does not require the use of specialized equipment or procedures. The purpose of the inspection is to provide the client with information regarding the general condition of the residence at the time of inspection. The inspector may provide a higher level of inspection performance than required by these standards of practice and may inspect components and systems in addition to those described by the standards of practice.

GENERAL LIMITATIONS

The inspector is not required to:

(A) inspect:

- (i) items other than those listed within these standards of practice;
- (ii) elevators;
- (iii) detached buildings, decks, docks, fences, or waterfront structures or equipment;
- (iv) anything buried, hidden, latent, or concealed;
- (v) sub-surface drainage systems;
- (vi) automated or programmable control systems, automatic shut-off, photoelectric sensors, timers, clocks, metering devices, signal lights, lightning arrestor system, remote controls, security or data distribution systems, solar panels, outdoor kitchens, gas grills (built-in or free standing), refrigerators (built-in or free standing), wine coolers, ice makers or smart home automation components; or refrigerators (built-in or free standing), wine coolers, ice makers or smart home automation components; or
- (vii) concrete flatwork such as; driveways, sidewalks, walkways, paving stones or patios;

- (i) past repairs that appear to be effective and workmanlike except as specifically required by these standards;
- (ii) cosmetic or aesthetic conditions; or
- (iii) wear and tear from ordinary use;

(C) determine:

- (i) insurability, warrantability, suitability, adequacy, compatibility, capacity, reliability, marketability, operating costs, recalls, counterfeit products, product lawsuits, life expectancy, age, energy efficiency, vapor barriers, thermostatic performance, compliance with any code, listing, testing or protocol authority, utility sources, or manufacturer or regulatory requirements except as specifically required by these standards;
- (ii) the presence or absence of pests, termites, or other wood-destroying insects or organisms;
- (iii) the presence, absence, or risk of asbestos, lead-based paint, MOLD, mildew, corrosive or contaminated drywall "Chinese Drywall" or any other environmental hazard, environmental pathogen, carcinogen, toxin, mycotoxin, pollutant, fungal presence or activity, or poison;
- (iv) types of wood or preservative treatment and fastener compatibility; or
- (v) the cause or source of a conditions;

(D) anticipate future events or conditions, including but not limited to:

- (i) decay, deterioration, or damage that may occur after the inspection;
- (ii) deficiencies from abuse, misuse or lack of use;
- (iii) changes in performance of any component or system due to changes in use or occupancy;
- (iv) the consequences of the inspection or its effects on current or future buyers and sellers;
- (v) common household accidents, personal injury, or death;
- (vi) the presence of water penetrations; or
- (vii) future performance of any item;
- (E) operate shut-off, safety, stop, pressure or pressure-regulating valves or items requiring the use of codes, keys, combinations, or similar devices;
- (F) designate conditions as safe;
- (G) recommend or provide engineering, architectural, appraisal, mitigation, physical surveying, realty, or other specialist services;
- (H) review historical records, installation instructions, repair plans, cost estimates, disclosure documents, or other reports;
- (I) verify sizing, efficiency, or adequacy of the ground surface drainage system;
- (J) verify sizing, efficiency, or adequacy of the gutter and downspout system;
- (K) operate recirculation or sump pumps;
- (L) remedy conditions preventing inspection of any item;
- (M) apply open flame or light a pilot to operate any appliance;
- (N) turn on decommissioned equipment, systems or utility services; or
- (O) provide repair cost estimates, recommendations, or re-inspection services.

THE CLIENT, BY ACCEPTING THIS PROPERTY INSPECTION REPORT OR RELYING UPON IT IN ANY WAY, EXPRESSLY AGREES TO THE SCOPE OF INSPECTION, GENERAL LIMITATIONS AND INSPECTION AGREEMENT INCLUDED IN THIS INSPECTION REPORT.

This inspection report is made for the sole purpose of assisting the purchaser to determine his and/or her own opinion of feasibility of purchasing the inspected property and does not warrant or guarantee all defects to be found. If you have any questions or are unclear regarding our findings, please call our office prior to the expiration of any time limitations such as option periods.

This report contains technical information. If you were not present during this inspection, please call the office to arrange for a consultation with your inspector. If you choose not to consult with the inspector, this inspection company cannot be held liable for your understanding or misunderstanding of the reports content.

The contents of this report are for the sole use of the client named above and no other person or party may rely on this report for any reason or purpose whatsoever without the prior written consent of the inspector who authored the report. Any person or party who chooses to rely on this report for any reason or purpose whatsoever without the express written consent of the inspector does so at their own risk and by doing so without the prior written consent of the inspector waives any claim of error or deficiency in this report.

This report is not intended to be used for determining insurability or warrantability of the structure and may not conform to the Texas Department of Insurance guidelines for property insurability. This report is not to be used by or for any property and/or home warranty company.

The digital pictures within this report are a representative sample of inaccessible areas, deficiencies or damages in place and should not be considered to show all of the inaccessible areas, deficiencies or damages observed. There will be inaccessible areas, deficiencies or damages not represented with digital imaging.

Report Identification: 69 Joyfull Way, Dallas, TX 75206 I=Inspected NI=Not Inspected **NP=Not Present D=Deficient** NI NP D

I. STRUCTURAL SYSTEMS

 \square \square \square A. Foundations

Type of Foundation(s): Slab on Ground

Comments:

Foundation Is Performing Adequately

In my opinion, the foundation appears to be providing adequate support for the structure at the time of this inspection. I did not observe any apparent evidence that would indicate the presence of adverse performance or significant deficiencies in the foundation. The interior and exterior stress indicators showed little affects of adverse performance and I perceived the foundation to contain no significant unlevelness after walking the 1st level floors.

Additional Observations and/or Comments:

Note: Tree(s) in close proximity of the foundation was observed. Client should consider the installation of a root barrier to reduce the possibility of damage to the foundation from tree roots and moisture removal.

Notice: This inspection is one of first impression and the inspector was not provided with any historical information pertaining to the structural integrity of the inspected real property. This is a limited cursory and visual survey of the accessible general conditions and circumstances present at the time of this inspection. Opinions are based on general observations made without the use of specialized tools or procedures. Therefore, the opinions expressed are one of apparent conditions and not of absolute fact and are only good for the date and time of this inspection.

The inspection of the foundation may show it to be providing adequate support for the structure or having movement typical to this region, at the time of the inspection. This does not guarantee the future life or failure of the foundation. The Inspector is not a structural engineer. This inspection is not an engineering report or evaluation and should not be considered one, either expressed or implied. If any cause of concern is noted on this report, or if you want further evaluation, you should consider an evaluation by an engineer of your choice.

Report Identification: 69 Joyfull Way, Dallas, TX 75206

I=Inspected NI=Not Inspected NP=Not Present D=Deficient

I NI NP D

 \square \square \square B. Grading and Drainage

Comments:

Grading & Drainage

All components were found to be performing and in satisfactory condition on the day of the inspection.

Gutter & Downspout System

• **Note:** The gutter downspouts should discharge water at least thirty-six inches (36") away from the foundation perimeter beam. Storm water should be encouraged to flow away from the structure at the points of discharge.

☐ ☐ ☐ C. Roof Covering Materials

Type(s) of Roof Covering: Composition

Viewed From: The roof was observed from ground level with binoculars. The two-story home roof level does not have readable safe access.

Comments:

Roof Covering

 This three story condominium unit does not have readable, safe roof access. It is recommended to have the builder and or builders roofer inspect prior to move in date, and correct and repairs that could be needed.



Notice: Life expectancy of the roofing material is not covered by this property inspection report. If any concerns exist about the roof covering life expectancy or potential for future problems, a roofing specialist should be consulted. The Inspector cannot offer an opinion or warranty as to whether the roof has leaked in the past, leaks now, or may be subject to future leaks, either expressed or implied.

The inspection of this roof may show it to be functioning as intended or in need of minor repairs. This inspection does not determine the insurability of the roof. You are strongly encouraged to have your Insurance Company physically inspect the roof, prior to the expiration of any time limitations such as option or warranty periods, to fully evaluate the insurability of the roof.

I=Inspected	NI=Not Inspected	NP=Not Present	D=Deficient	
I NI NP D				

\square \square \square \square D. Roof Structures and Attics

Viewed From: From Interior of Attic

Approximate Average Depth of Insulation: 13+"

(Note: Generally recommended depth of attic floor insulation is approximately 10+ inches to achieve a

R30 rating.)

Insulation Type: Loose Filled

Description of Roof Structure: Truss Assembly

Attic Accessibility: Partial

Comments:

Roof Structure

All components were found to be performing and in satisfactory condition on the day of the inspection.

Attic Ventilation

• The roof structure attic space ventilation appears to be marginal at the time of this inspection. It is recommended to increase the amount of lower and upper ventilation to help prevent heat buildup in the attic space area.

Attic Insulation

All components were found to be performing and in satisfactory condition on the day of the inspection.



NI=Not Inspected

NP=Not Present

D=Deficient

NI NP D

Upstairs Stairwell Attic Ladder

• The attic ladder was observed to have gaps at the joints when the ladder was fully extended. Improvements are recommended for reasons of safety.





E. Walls (Interior and Exterior)

Comments:

Description of Exterior Cladding: Wood Type Veneer

Interior Walls & Surfaces

Note: There is evidence of painting and patching to the interior finish and prior interior finish repairs. This condition could limit the Inspectors visual observations and ability to render accurate opinions as to the performance of the structure.

Note: Nail heads were observed to be pushing through the interior finish in one or more locations.

- The wall texture has some deterioration and/or damage in the garage, stairway, various locations throughout the house and paint touch ups are recommended.
- Wall surface damage was observed in the kitchen.




NI=Not Inspected

NP=Not Present

D=Deficient

NI NP D





Exterior Walls & Surfaces

All components were found to be performing and in satisfactory condition on the day of the inspection.







I=Inspected NI=Not Inspected NP=Not Present D=Deficient

I NI NP D


 \square \square \square \square \square \square F. Ceilings and Floors

Comments:

Ceilings

Note: There is evidence of painting and patching to the interior finish and prior interior finish repairs. This condition could limit the Inspectors visual observations and ability to render accurate opinions as to the performance of the structure.

• Ceiling joint cracks were observed in the family room.



Floors

- The study closet door area is missing a transition strip. There should be a transition/threshold where the elevations of multiple floor surfaces are different.
- The floor covering was observed to be damaged in the kitchen.
- Note: Some cracking of the garage concrete floor finish was observed.



NI=Not Inspected

NP=Not Present

D=Deficient

NI NP D





G. Doors (Interior and Exterior)

Comments:

Interior Doors

All components were found to be performing and in satisfactory condition on the day of the inspection.

Exterior Doors

Weather-stripping improvements are recommended for the front entry exterior door(s).



NI=Not Inspected

NP=Not Present

D=Deficient

NI NP D

Overhead Garage Door

All components were found to be performing and in satisfactory condition on the day of the inspection.

Garage Entry Door

• The garage entry door is not equipped with a self-closing device.



H. Windows


Comments:

Window Screens

• There are no window screens in place at the time of this inspection.

Windows

• One or more of the windows were observed to be extremely stiff and very hard to operate in the breakfast area.



Report Identification: 69 Joyfull Way, Dallas, TX 75206

I=Inspected					NI=Not Inspected	NP=Not Present	D=Deficient
I	NI	NP	D				
V				I.	Stairways (Interior and External Comments:	erior)	
					All components were found to	be performing and in satisfac	ctory condition on the day of the inspection.
	☑	☑		J.	Fireplaces and Chimneys Comments:		
V				K.	Porches, Balconies, Decks, a Comments:	nd Carports	
					Porches All components were found to	be performing and in satisfac	ctory condition on the day of the inspection.
					Balcony All components were found to	be performing and in satisfac	ctory condition on the day of the inspection.

Driveway

• Minor cracks and/or deficiencies were observed in the driveway.



Report Identification: 69 Joyfull Way, Dallas, TX 75206

I=Inspected NI=Not Inspected NP=Not Present D=Deficient

I NI NP D

II. ELECTRICAL SYSTEMS

A. Service Entrance and Panels

Comments:

Panel Box

Box Rating and/or Main Disconnect Rating: 200 amps

Box Location: Garage

Cabinet Manufacturer: Square D Branch Circuit Wire Type: Copper

All components were found to be performing and in satisfactory condition on the day of the inspection.



Service Entrance

All components were found to be performing and in satisfactory condition on the day of the inspection.

Grounding / Bonding

All components were found to be performing and in satisfactory condition on the day of the inspection.

lacktriangleq B. Branch Circuits, Connected Devices, and Fixtures *Type of Wiring*: Copper

Comments:

Receptacle Outlets

- One or more of the receptacles is missing its cover plate in the garage.
- One or more of the receptacles were observed to be loose at the wall mount in the study.

NI=Not Inspected

NP=Not Present

D=Deficient

NI NP D

Switches

The switch is poorly located at the wall mount in the master bedroom closet.



Fixtures

• Some of the light fixtures have been removed and/or missing. The missing fixtures should be replaced where the junction boxes have been covered.





Smoke Alarms

Note: It is recommended to replace the batteries in all of the smoke detectors once a year for reasons of safety.

Note: Due to location, height or conditions outside the control of the inspector, one or more of the smoke alarms were inaccessible and could not be tested at the time of this inspection.

All components were found to be performing and in satisfactory condition on the day of the inspection.

Carbon Monoxide Alarms

All components were found to be performing and in satisfactory condition on the day of the inspection.

I=Inspected NI=Not Inspected NP=Not Present D=Deficient

I NI NP D

III. HEATING, VENTILATION AND AIR CONDITIONING SYSTEMS

☑ □ □ A. Heating Equipment

Type of Systems: Energy Sources: Comments:

Central Heating System - Energy Source: Electric

Brand Name: Trane

This component appears to be performing adequately at the time of this inspection. It is achieving an operation, function, or configuration consistent with accepted industry practices for its age.





I=Inspected NI=Not Inspected NP=Not Present D=Deficient

I NI NP D

☑ □ □ ☑ B. Cooling Equipment

Type of Systems: Comments:

Central Cooling System

Today's Temperature Differential (Delta-T): 15

Approximate System Age: 2019 Approximate System SEER: 14 Approximate System Size: 3.5 ton

Filter Size: 20 x 24 x 2 Location: At Attic Unit

Brand Name: Trane

The HVAC system and equipment needs to be checked and serviced by a Qualified / Licensed HVAC Technician. The observations made to support the rendering of this opinion are listed but may not be limited to the following:

- The electrical service disconnect is installed behind the outside condenser/coil. This does not meet the clearance requirements of the National Electrical Code or the International Residential Code and should be corrected as necessary.
- Damaged, deteriorated and/or missing insulation on the refrigerant lines should be repaired or replaced at the outside condenser.
- **Note:** The heavy foliage at and around the outside condenser/coils should be trimmed back a minimum of 18-inches to help improve air circulation.
- **Note:** The auxiliary/secondary drain pan under the coil housing should be free of all debris. The debris in the pan could clog the drain line and cause water to leak to the interior of the house.




NI=Not Inspected

NP=Not Present

D=Deficient

NI NP D

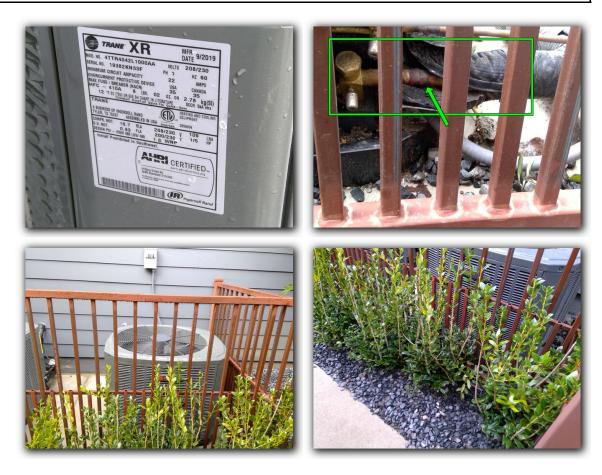

Note: When D (**D** = **Deficient**) is checked, it is recommended that this item be fully investigated by a Qualified / Licensed HVAC Technician, prior to the expiration of any time limitations such as option or warranty periods, to fully evaluate the integrity of the equipment.

Notice: Temperature differential readings (Delta-T) are an accepted industry standard of practice for testing the proper operation of the cooling system. Our company policy normal acceptable range is considered approximately between 15 to 20 degrees °F total difference (Delta-T) measured between the return air and supply air within close proximity of the related coils of the system being evaluated. Conditions such as but not limited to; excessive humidity, high or low outdoor temperatures or restricted airflow may indicate abnormal operation even through the equipment is functioning basically as designed and occasionally may indicate normal operation in spite of an equipment malfunction. The inspector will not be able to anticipate future events, conditions or changes in performance of any component or system due to changes in use or occupancy. The inspector makes no guarantee or warranty, express or implied, as to future performance of any item, system or component.

☑ □ □ □ C. Duct Systems, Chases, and Vents Comments:

All components were found to be performing and in satisfactory condition on the day of the inspection.

I=Inspected NI=Not Inspected NP=Not Present D=Deficient

I NI NP D

IV. PLUMBING SYSTEM

\square \square \square A. Plumbing Supply, Distribution Systems and Fixtures

Location of water meter: Within 5-feet of Front Curb Location of main water supply valve: Unable to Locate a Main Supply Valve Static water pressure reading: 50 to 60 psi

Comments:

Laundry Connections

All components were found to be performing and in satisfactory condition on the day of the inspection.

Kitchen Sink

All components were found to be performing and in satisfactory condition on the day of the inspection.

Upstairs Rear Middle Bedroom Bathroom

Bathtub

- The bathtub shower head diverter is not functioning properly.
- The shower spout is leaking at the neck connection.

Lavatory / Sink

• The stopper does not appear to be functioning properly.





NI=Not Inspected

NP=Not Present


D=Deficient

NI NP D

Master Bathroom

Shower

• The faucet assembly is not sealed at the wall. This condition has the potential to allow water to leak back into the wall cavity.





Half Bath

All components were found to be performing and in satisfactory condition on the day of the inspection.

Notice: The Inspector has attempted to discover and report conditions requiring further evaluation or repair. However; determining the condition of any component that is not visible and/or accessible, such as plumbing components that are buried, beneath the foundation, located within construction voids or otherwise concealed, and reporting any deficiency that does not appear or become evident during our limited cursory and visual survey is outside the scope of this inspection. The inspector will not be able to anticipate future events, conditions or changes in performance of any component or system due to changes in use or occupancy. The inspector makes no guarantee or warranty, express or implied, as to future performance of any item, system or component.

Report Identification: 69 Joyfull Way, Dallas, TX 75206

I=Inspected NI=Not Inspected NP=Not Present D=Deficient

I NI NP D

B. Drains, Wastes, and Vents

Comments:

All components were found to be performing and in satisfactory condition on the day of the inspection.

Notice: Reporting the condition of drains, wastes and vent piping that is not completely visible and/or accessible or; reporting any defect or deficiency that requires extended use of the system to develop or does not become evident during our limited cursory and visual survey is outside the scope of the inspection. This is a limited cursory and visual survey of the accessible general conditions and circumstances present at the time of this inspection. Opinions are based on general observations made without the use of specialized tools or procedures. Therefore, the opinions expressed are one of apparent conditions and not of absolute fact and are only good for the date and time of this inspection. The inspector will not be able to anticipate future events, conditions or changes in performance of any component or system due to changes in use or occupancy. The inspector makes no guarantee or warranty, express or implied, as to future performance of any item, system or component.

I=Inspected NI=Not Inspected NP=Not Present D=Deficient

I NI NP D

☑ □ □ □ C. Water Heating Equipment

Energy Sources: Capacity: Comments:

Water Heater - Energy Source: Electric

Location: Garage

Approximate Capacity: 50 Gallons

Approximate Age: 2019
Brand Name: Lochinvar

This component appears to be performing adequately at the time of this inspection. It is achieving an operation, function, or configuration consistent with accepted industry practices for its age.

Additional Observations and/or Comments:

• **Note:** The debris in the water heater pan should be cleaned out to help prevent the pan drain line from being clogged.







Report Identification: 69 Joyfull Way, Dallas, TX 75206

I=Inspected NI=Not Inspected NP=Not Present D=Deficient

I NI NP D

D. Hydro-Massage Therapy Equipment

Comments:

Report Identification: 69 Joyfull Way, Dallas, TX 75206

I=Inspected NI=Not Inspected NP=Not Present D=Deficient				D=Deficient			
I	NI	NP	D				
V				A.	Dishwashers Comments: Brand Name: KitchenAid	V. APPLIANCES	
					This component appears to be	performing adequately at the	time of this inspection.
				В.	Food Waste Disposers <i>Comments</i> :		
					This component appears to be	performing adequately at the	time of this inspection.
				C.	Range Hood and Exhaust Sy Comments: • The range exhaust vent fil		
✓				D.	Ranges, Cooktops, and Oven Comments: Range Brand Name: Kitchen A. This component appears to be	Aid	e time of this inspection.

This component appears to be performing adequately at the time of this inspection.

Brand Name: Kitchen Aid

E. Microwave Ovens Comments:

NI=Not Inspected

NP=Not Present

D=Deficient

NI NP D



☑ □ □ F. Mechanical Exhaust Vents and Bathroom Heaters

Comments:

This component appears to be performing adequately at the time of this inspection.

☑ □ □ ☑ G. Garage Door Operators

Comments:

When an automatic garage door opener is in use, the manual lock should be disabled or removed.



☑ □ □ □ H. Dryer Exhaust Systems

Comments:

This component appears to be performing adequately at the time of this inspection.

INSPECTION AGREEMENT PLEASE READ THIS AGREEMENT CAREFULLY BEFORE SIGNING

This Inspection Agreement (herein after known as the Agreement) is entered into on this day, 04/09/2020, between Bob Buyer (herein known as the Client) and SiteGuard Inspection Services (herein known as the Inspector) for the purpose of performing a general property condition inspection concerning 69 Joyfull Way (herein known as the property).

I. SCOPE OF SERVICES

- A. A real estate inspection is a non-technically exhaustive, limited visual survey and basic performance evaluation of the systems and components of a building using normal controls and does not require the use of specialized equipment or procedures. The purpose of the inspection is to provide the Client with information regarding the general condition of the Property at the time of inspection.
- B. In exchange for the inspection fee (\$) paid by the Client, the Inspector agrees to provide the Client with an Inspection Report setting out the Inspector's professional opinions concerning the condition of the Property further described in the report. The inspection will be performed in accordance with the Standards of Practice promulgated by the Texas Real Estate Commission. Inspector will attempt to identify major defects and problems with the Property. However, Client acknowledges that the Inspection Report may not identify all defects or problems.
- C. The inspection is limited to those items which are easily accessible, seen, viewed or capable of being approached, entered and/or operated by the Inspector at the time of the inspection as set out in the Inspection Report. The Inspector will not climb over obstacles, move furnishings or large, heavy, or fragile objects, remove walls, floors, wall coverings, floor coverings and other obstructions in order to inspect concealed items. The inspector will not turn on decommissioned equipment, systems, utility services. Systems, components and conditions which are not specifically addressed in the Inspection Report are excluded.
- D. The Inspection Report may indicate one of the following opinions of the Inspector regarding a particular item:
 - 1. The item is performing its intended function, achieving an operation, function or configuration relative to accepted industry standard practices with consideration of age and normal wear and tear from ordinary use at the time of the inspection;
 - 2. The item is in need of replacement, maintenance or repair; or
 - 3. Further evaluation by an expert is recommended.

II. INSPECTION REPORT

- A. The Inspection Report provided by the Inspector will contain the Inspector's professional, good-faith opinions concerning the need for repair or replacement of certain observable items. All statements in the report are the Inspector's opinions and should not be construed as statements of fact or factual representations concerning the Property. By signing this Agreement, the Client understands that the services provided by the Inspector fall within the Professional Services Exemption of the Texas Deceptive Trade Practices Act ("DTPA") and agrees that no cause of action exists under the DTPA related to the services provided.
- B. Unless specifically stated, the report WILL NOT INCLUDE and should not be read to indicate OPINIONS AS TO;
 - 1. the presence, absence, or risk of environmental conditions such as asbestos, lead-based paint, **MOLD**, mildew, corrosive or contaminated drywall "Chinese Drywall" or any other environmental hazard, environmental pathogen, carcinogen, toxin, mycotoxin, pollutant, fungal presence or activity, poison, presence of toxic or hazardous waste or substances;
 - 2. presence or absence of pests, termites, or other wood-destroying insects or organisms;
 - 3. <u>COMPLIANCE WITH</u> compliance with any ordinances, statutes or restrictions, <u>CODE</u>, listing, testing or protocol authority, utility sources, property association guidelines or requirements, manufacturer or regulatory requirements;
 - 4. insurability, efficiency warrantability, suitability, adequacy, compatibility, capacity, durability, quality reliability, marketability, operating costs, recalls, counterfeit products, product lawsuits, age, energy efficiency; or
 - 5. anticipate future life or future events or changes in performance of any item inspected.
- C. The Inspection Report is not a substitute for disclosures by sellers and real estate agents. Said disclosure statements should be carefully investigated for any material facts that may influence or effect the desirability and/or market value of the Property.
- D. As noted above, the Inspection Report may state that further evaluation of certain items is needed by an expert in the field of the item inspected. By signing this Agreement, Client acknowledges that qualified experts may be needed to further evaluate such items as structural systems, foundations, grading, drainage, roofing, plumbing, electrical systems, HVAC, appliances, sprinkler systems pool system and components, fire/smoke detection systems, septic systems and other observable items as noted in the report. Any such follow-up should take place prior to the expiration of any time limitations such as option or warranty periods.

Report Identification: 69 Joyfull Way, Dallas, TX 75206

III. DISCLAIMER OF WARRANTIES

The inspector makes no guarantee or warranty, express or implied, as to any of the following:

- 1. That all defects have been found or that the Inspector will pay for repair of undisclosed defects;
- 2. That any of the items inspected are designed or constructed in a good and workmanlike manner;
- 3. That any of the items inspected will continue to perform in the future as they are performing at time of the inspection; and
- 4. That any of the items inspected are merchantable or fit for any particular purpose.

IV. LIMITATION OF LIABILITY

BY SIGNING THIS AGREEMENT, CLIENT ACKNOWLEDGES THAT THE INSPECTION FEE PAID TO THE INSPECTOR IS NOMINAL GIVEN THE RISK OF LIABILITY ASSOCIATED WITH PERFORMING HOME INSPECTIONS IF LIABILITY COULD NOT BE LIMITED. CLIENT ACKNOWLEDGES THAT WITHOUT THE ABILITY TO LIMIT LIABILITY, THE INSPECTOR WOULD BE FORCED TO CHARGE CLIENT MUCH MORE THAN THE INSPECTION FEE FOR THE INSPECTOR'S SERVICES. CLIENT ACKNOWLEDGES BEING GIVEN THE OPPORTUNITY TO HAVE THIS AGREEMENT REVIEWED BY COUNSEL OF HIS OR HER OWN CHOOSING AND FURTHER ACKNOWLEDGES THE OPPORTUNITY OF HIRING A DIFFERENT INSPECTOR TO PERFORM THE INSPECTION. BY SIGNING THIS AGREEMENT, CLIENT AGREES TO LIABILITY BEING LIMITED TO THE AMOUNT OF THE INSPECTION FEE PAID BY THE CLIENT. \$

V. DISPUTE RESOLUTION

In the event a dispute arises regarding an inspection that has been performed under this agreement, the Client agrees to notify the Inspector within ten (10) days of the date the Client discovers the basis for the dispute so as to give the Inspector a reasonable opportunity to reinspect the property. Client agrees to allow reinspection before any corrective action is taken. Client agrees not to disturb or repair or have repaired anything which might constitute evidence relating to a complaint against the Inspector. Client further agrees that the Inspector can either conduct the reinspection himself or can employ others (at Inspector's expense) to reinspect the property, or both. In the event a dispute cannot be resolved by the Client and the Inspector, the parties agree that any dispute or controversy shall be resolved by mandatory and binding arbitration administered by the American Arbitration Association ("AAA") pursuant to Chapter 171 of the Texas Civil Practice & Remedies Code and in accordance with this arbitration agreement and the commercial arbitration rules of the AAA.

VI. ATTORNEY'S FEES

The Inspector and the Client agree that in the event any dispute or controversy arises as a result of this Agreement, and the services provided hereunder, the prevailing party in that dispute shall be entitled to recover all of the prevailing party's reasonable and necessary attorneys' fees and costs incurred by that party.

VII. EXCLUSIVITY

The Inspection Report is to be prepared exclusively for the Client and is not transferable to anyone in any form. Client gives permission for the Inspector to discuss report findings with real estate agents, specialists, or repair persons for the sake of clarification. A copy of the Inspection Report may be released to the buyers Real Estate Agent.

BY MY SIGNATURE BELOW, I ACKNOWLEDGE THAT I HAVE READ THIS CONTRACT AND THAT THE INSPECTOR DID NOT COERCE, PRESSURE OR RUSH ME TO EXECUTE THIS CONTRACT WITHOUT OPPORTUNITY TO FULLY REVIEW THE CONTRACT AND IF NECESSARY HAVE THE CONTRACT REVIEWED BY AN ATTORNEY; THAT INSPECTOR AGREED TO RESCHEDULE THE INSPECTION IN THE EVENT I REQUIRED ADDITIONAL TIME TO REVIEW THE CONTRACT; THAT I UNDERSTAND THE TERMS AND CONDITIONS AND THAT I AGREE TO BE BOUND BY THESE TERMS AND CONDITIONS. IF CLIENT IS MARRIED, CLIENT REPRESENTS THAT THIS OBLIGATION IS A FAMILY OBLIGATION INCURRED IN THE INTEREST OF THE FAMILY.

Client Signature:	Date: <u>04/09/2020</u>
Inspector: Nathan Ross	

REPORT SUMMARY

The "Report Summary" section is intended to be a tool to assist our clients and their representative(s) in preparing a repair request, if and when applicable. <u>THIS IS NOT A LIST OF MANDATORY REPAIRS BUT A LIST OF SUGGESTED REPAIRS OR UPGRADES NEEDED IN THE SHORT TERM.</u>

The Report Summary is intended to follow the flow of the main body of the Property Inspection Report and <u>IS NOT</u> a suggested priority repair list. The order of repair priority is left up to the sole discretion of the client and your Inspector will not be able to assist you specifying order of importance. Further, this summary contains only those items identified as "Deficient". There may be other items listed in the full body of the Property Inspection Report that could be important to you and you may consider adding to your repair request if and when applicable.

<u>You should read and understand the entire Property Inspection Report prior to completing any repair request.</u> This report contains technical information, if you do not understand or are unclear about some of the information contained in the body of this report; please call the office to arrange for a verbal consultation with your inspector prior to the prior to the expiration of any time limitations such as option or warranty periods.

- Wall surface damage was observed in the kitchen.
- The floor covering was observed to be damaged in the kitchen.
- Weather-stripping improvements are recommended for the front entry exterior door(s).
- The garage entry door is not equipped with a self-closing device.

Service Entrance

Grounding / Bonding

- One or more of the receptacles is missing its cover plate in the garage.
- The switch is poorly located at the wall mount in the master bedroom closet.
- Some of the light fixtures have been removed and/or missing. The missing fixtures should be replaced where the junction boxes have been covered.
- The electrical service disconnect is installed behind the outside condenser/coil.

Bathtub

- The bathtub shower head diverter is not functioning properly.
- The shower spout is leaking at the neck connection.

Lavatory / Sink

• The stopper does not appear to be functioning properly.

Shower

• The range exhaust vent filter is missing.

TEXAS OFFICIAL WOOD DESTROYING INSECT REPORT

Client Present during Inspection: No

Termite Report is Paid in Full

Termite Warranty Offered: No

(1A.) Name of Inspection Company: Insect Detect Termite and Pest (IC.) 3834 Lucena Ct Grand Prairie, Tx75052 972-979-7346 (1B.) SPCS Business License Number#8025433 Seller Agent Buyer Management Co. Other 4A. Bob Buyer Name of Person Purchasing Inspection 69 Joyfull Way Dallas, TX 75206 Inspected Address Telephone No. 1D. Nathan Ross #0605004 1E. Certified Applicator (check one) \square Name of Inspector (Please Print) Technician 2. Unknown 3. Thursday, February 20, 2020 Inspection Date Case Number (VA/FHA/Other) 4B. Not Determind Owner/Seller 4C. REPORT FORWARDED TO: Title Company or Mortgagee Purchaser of Service Seller Agent (Under the Structural Pest Control Service of the Texas Department of Agriculture regulations only the purchaser of the service is required to receive a copy)

SCOPE OF INSPECTION / AGREEMENT

- This inspection covers only the multi-family structure, primary dwelling or place of business. Sheds, detached garages, lean-tos, fences, guest A. houses or any other structure will not be included in this inspection report unless specifically noted in Section 5 of this report.
- В. This inspection is limited to those parts of the structure(s) that are visible and accessible at the time of the inspection. Examples of inaccessible areas include but are not limited to (1) areas concealed by wall coverings, furniture, equipment and stored articles and (2) any portion of the structure in which inspection would necessitate removing or defacing any part of the structure(s) (including the surface appearance of the structure). Inspection does not cover any condition or damage which was not visible in or on the structure(s) at time of inspection but which may be revealed in the course of repair or replacement work.
- C. Due to the characteristics and behavior of various wood destroying insects, it may not always be possible to determine the presence of infestation without defacing or removing parts of the structure being inspected. Previous damage to trim, wall surface, etc., is frequently repaired prior to the inspection with putty, spackling, tape or other decorative devices. Damage that has been concealed or repaired may not be visible except by defacing the surface appearance. The WDI inspecting company cannot guarantee or determine that work performed by a previous pest control company, as indicated by visual evidence of previous treatment, has rendered the pest(s) inactive.
- D. If visible evidence of active or previous infestation of listed wood destroying insects is reported, it should be assumed that some degree of damage is present.
- E. If visible evidence is reported, it does not imply that damage should be repaired or replaced. Inspectors of the inspection company usually are not engineers or builders qualified to give an opinion regarding the degree of structural damage. Evaluation of damage and any corrective action should be performed by a qualified expert.
- THIS IS NOT A STRUCTURAL DAMAGE REPORT OR A WARRANTY AS TO THE ABSENCE OF WOOD DESTROYING F. INSECTS.

Property was Vacant

- G. If termite treatment (including pesticides, baits or other methods) has been recommended, the treating company must provide a diagram of the structure(s) inspected and proposed for treatment, label of pesticides to be used and complete details of warranty (if any). At a minimum, the warranty must specify which areas of the structure(s) are covered by warranty, renewal options and approval by a certified applicator in the termite category. Information regarding treatment and any warranties should be provided by the party contracting for such services to any prospective buyers of the property. The inspecting company has no duty to provide such information to any person other than the contracting party.
- H. There are a variety of termite control options offered by pest control companies. These options will vary in cost, efficacy, areas treated, warranties, treatment techniques and renewal options.
- I. There are some specific guidelines as to when it is appropriate for corrective treatment to be recommended. Corrective treatment may only be recommended if (1) there is visible evidence of an active infestation in or on the structure, (2) there is visible evidence of a previous infestation with no evidence of a prior treatment.
- J. If treatment is recommended based solely on the presence of conducive conditions, a preventive treatment or correction of conducive conditions may be recommended. The buyer and seller should be aware that there may be a variety of different strategies to correct the conducive condition(s). These corrective measures can vary greatly in cost and effectiveness and may or may not require the services of a licensed pest control operator. There may be instances where the inspector will recommend correction of the conducive conditions by either mechanical alteration or cultural changes. Mechanical alteration may be in some instances the most economical method to correct conducive conditions. If this inspection report recommends any type of treatment and you have any questions about this, you may contact the inspector involved, another licensed pest control operator for a second opinion, and/or the Structural Pest Control Service of the Texas Department of Agriculture.

The structure(s) listed below were inspected in accordance with the official inspection procedures adopted by the Texas Structural Pest Control Service. This report is made subject to the conditions listed under the Scope of Inspection. A diagram must be attached including all structures inspected.

5. List structure(s) inspected that may include residence, detached garages and other structures on the property. (Refer to Part A, Scope of Inspection):								
☑ Main House (Excluding all Detached Structures, Sheds, Shrubs, Trees, Barns, Fences and Decks)								
_	☐Main House & Detached Garage (Excluding all other Detached Structures, Sheds, Shrubs, Trees Barns, Fences and Decks)							and Decks)
☐ Other Inspected Struc	tures:							
6A. Were any areas of the prope (Refer to Part B & C, Scope of I				Yes 🗹	No 🗆			
6B. The obstructed or inaccessil	ble areas includ	le but are not limited to the f	following:					
Attic		Plumbing Areas	$\overline{\checkmark}$	Planter box al	outting structure		Slab Joints	$\overline{\checkmark}$
Attic Partially Accessible	$\overline{\checkmark}$	Bath-trap(s)	$\overline{\checkmark}$	Below or Beh	ind High Soil Grade		Cracks in Slab	$\overline{\checkmark}$
Insulated areas of attic	\checkmark	Construction Voids	$ \mathbf{V}$	Wood Pile in	Contact with Structure		Crawl Space	
Inside Eaves	\checkmark	Recent Renovation(s)		Behind Person	nal Effects / Furniture		Sub Floors	$\overline{\checkmark}$
Deck		Blocked/Stored Areas	$\overline{\checkmark}$	Debris Piled I	Next to Structure		Weepholes	
Behind Storage in Garage		Under Floor Covering		Crawl Space	Partially Accessible		Heavy Foliage	
Raised Concrete, Brick and/or Stone at Patio/Porch(s)				Behind Found	ltion Beam Cosmetic Repair	$\overline{\checkmark}$	Behind Cabinter	y 🗹
Behind Wood Paneling (Wall Covering)				Behind Bathro	oom Tile Enclosures			
Foundation Corner Pops				Foundation P	lumbing Penetrations			
Other Specify: adj	acent no	access						

SPCS/T-4 (Rev. 09/01/07) Buyer's Initials ______

Yes ☑ No □	
Wood Pile in Contact with Structure or withi Wooden Fence in Contact with the Structure Footing soil line too high (L) Tree Branches in Contact with Roof Structur Flowerbed Wood Formers within Dripline (F	re (TB)
Yes	Previous Treatment Yes
Yes 🗆	No 🗹
Yes 🔲	No 🗹 No 🗹
Bait C od C N/A Name of Pesticide, B.	Other ait or Other Method
	Wood Pile in Contact with Structure or with Wooden Fence in Contact with the Structure Footing soil line too high (L) Tree Branches in Contact with Roof Structure Flowerbed Wood Formers within Dripline (I Previous Infestation Yes No Y Yes No Y

SPCS/T-4 (Rev. 09/01/07) Buyer's Initials ______

Diagram of Structure(s) Inspected


Foundation Type: Slab on Ground Primary Use: Residential

The inspector must draw a diagram including approximate perimeter measurements and indicate active or previous infestation and type of insect by using the following codes:

(E)=Evidence of infestation; (A)=Active; (P)=Previous; (D)=Drywood Termites; (S)=Subterranean Termites; (D)=Drywood Termites; (D)=Dr

(F)=Formosan Termites; (C)=Conducive Conditions; (B)=Wood Boring Beetles; (H)=Carpenter Ants;

(X)=Drill Holes; (BS)=Bait Stations; Other(s) - Specify _

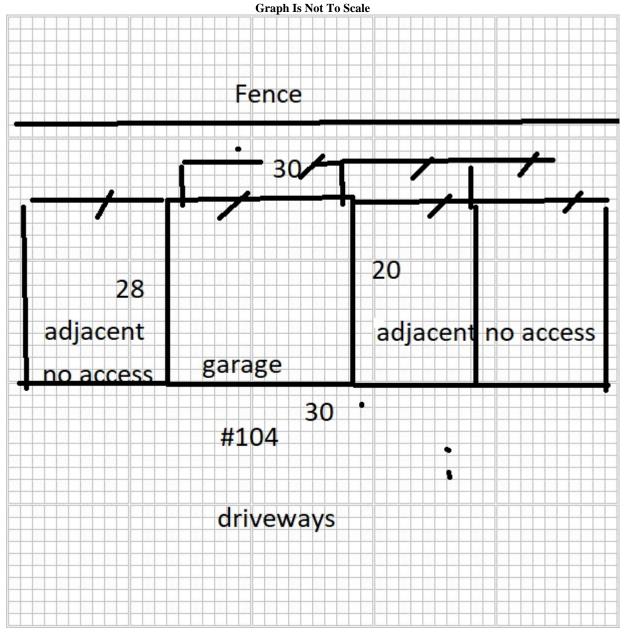

Additional Comments There is no visible evidence of active wood destroying insects found at the time of this inspection.

Notice to Client: There is always a possibility of the presence of undetectable activity of wood destroying insects. THIS IS NOT A STRUCTURAL DAMAGE REPORT OR A WARRANTY AS TO THE ABSENCE OF WOOD DESTROYING INSECTS. If visible evidence of active or previous infestation of listed wood destroying insects is reported, it should be assumed that some degree of damage is present, whether visible or non-visible.

SPCS/T-4 (Rev. 09/01/07) Buyer's Initials ______

TEXAS OFFICIAL WOOD DESTROYING INSECT REPORT

Neither I nor the company for which I am acting have had, presently have, or contemplate having any interest in the property. I do further state that neither I nor the company which I am acting is associated in any way with any party to the transaction.

Signatures: Nathan Ross	Notice of Inspection Was Posted At or Near
11A. Nathan Ross #0821398 Inspector Approved: 11B. Nathan Ross #0821398 / Thursday, February 20, 2020	12A. Electric Breaker Box Water Heater Closet Bath Trap Access Beneath the Kitchen Sink 12B. Date Posted 02/20/2020
Certified Applicator and Certified Applicator License Number	Date
~	
Signature of Purchaser of Property or their Designee	Date

SPCS/T-4 (Rev. 09/01/07) Buyer's Initials _____

The digital pictures within this report are a representative sample of active/previous wood destroying insects, locations of active/previous infestations, inaccessible areas, conducive conditions, deficiencies or damages in place and should not be considered to show all. There will be active/previous wood destroying insects, locations of active/previous infestations, inaccessible areas, conducive conditions, deficiencies or damages not represented with digital imaging.

